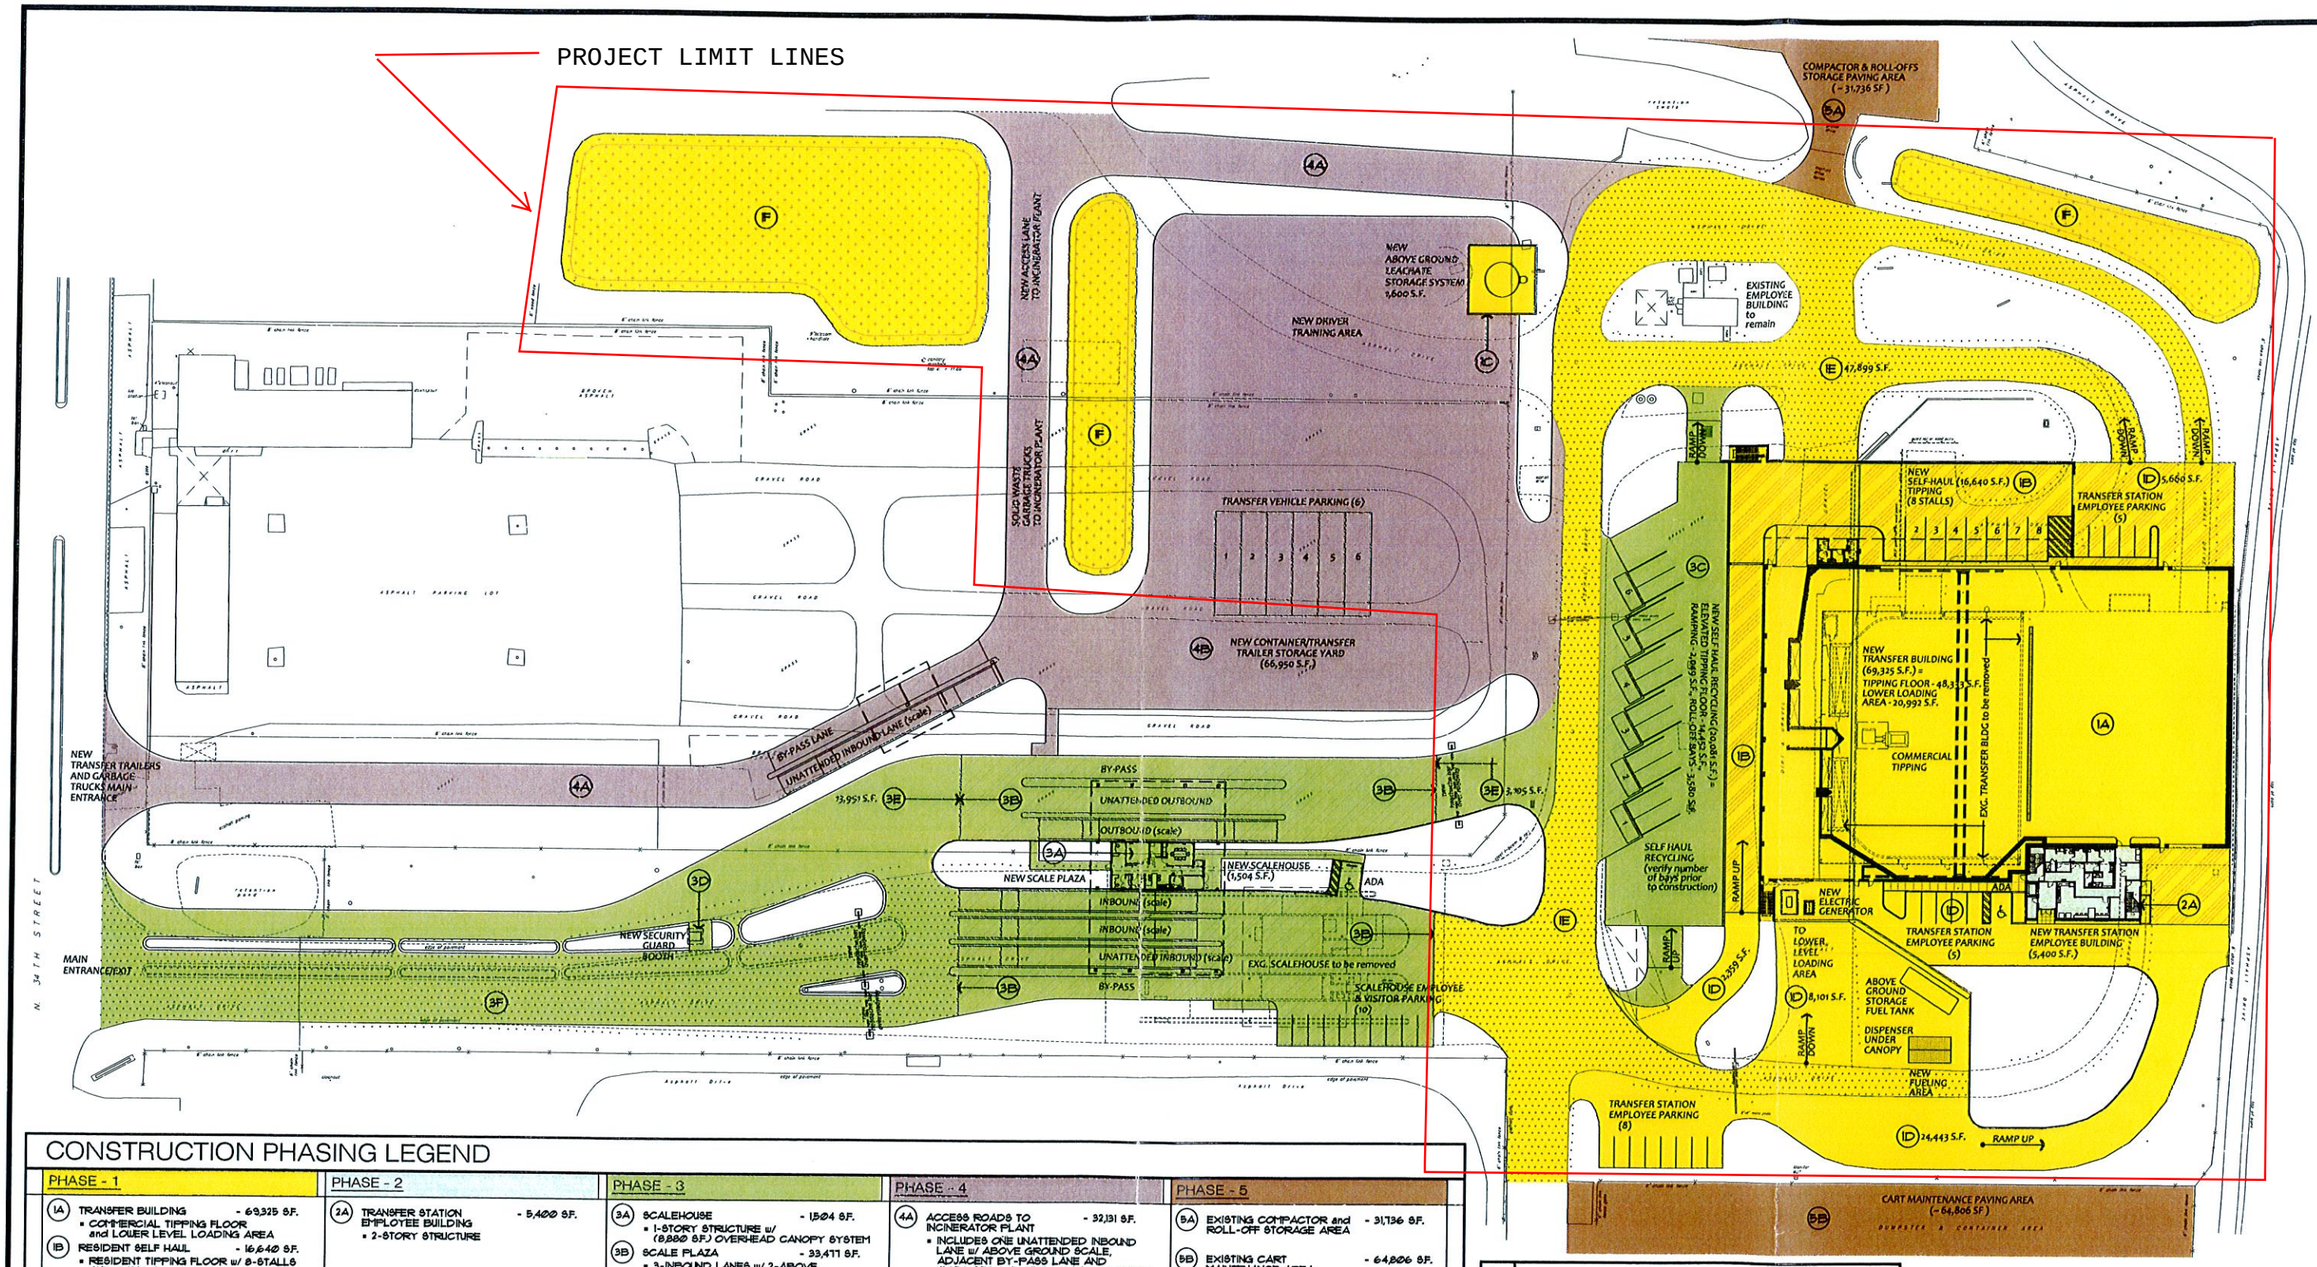

CONSTRUCTION PHASING LEGEND

PHASE - 1

- (1A) TRANSFER BUILDING - 69,325 S.F.
  - COMMERCIAL TIPPING FLOOR and LOWER LEVEL LOADING AREA
- (1B) RESIDENT SELF HAUL - 16,640 S.F.
  - RESIDENT TIPPING FLOOR w/ 8-STALLS AND RAMP APPROACH TO THE WEST OF TRANSFER BUILDING
- (1C) ABOVE GROUND LEACHATE STORAGE SYSTEM - 1,600 S.F.
- (1D) NEW PAVEMENT - 40,563 S.F.
- (1E) EXISTING ROADS TO REMAIN (RE-SURFACE) - 47,899 S.F.
- (1F) NEW PONDS (3 TOTAL) - 40,223 S.F.

PHASE - 2

- (2A) TRANSFER STATION EMPLOYEE BUILDING - 5,400 S.F.
  - 2-STORY STRUCTURE

PHASE - 3

- (3A) SCALEHOUSE - 1,504 S.F.
  - 1-STORY STRUCTURE w/ (8,880 S.F.) OVERHEAD CANOPY SYSTEM
- (3B) SCALE PLAZA - 33,477 S.F.
  - 3-INBOUND LANES w/ 2-ABOVE GROUND SCALES, 2-OUTBOUND LANES w/ 1-ABOVE GROUND SCALE and 2 BY-PASS LANES
- (3C) SELF HAUL RECYCLING - 20,081 S.F.
  - 6-BAY 'Z' WALL ARRANGEMENT FOR ROLL-OFF DUMPSTERS. INCLUDES LEACHATE COLLECTION SYSTEM.
- (3D) SECURITY GUARD BOOTH - 220 S.F.
- (3E) NEW PAVEMENT - 17,056 S.F.

PHASE - 4

- (4A) ACCESS ROADS TO INCINERATOR PLANT - 32,131 S.F.
  - INCLUDES ONE UNATTENDED INBOUND LANE w/ ABOVE GROUND SCALE, ADJACENT BY-PASS LANE AND (1,656 S.F.) OVERHEAD CANOPY SYSTEM
- (4B) CONTAINER/TRANSFER TRAILER STORAGE YARD - 66,950 S.F.
  - 6-PARKING STALLS w/ LEACHATE COLLECTION SYSTEM.
- (3F) EXISTING ROADS TO REMAIN (RE-SURFACE) - 23,635 S.F.

PHASE - 5

- (5A) EXISTING COMPACTOR and ROLL-OFF STORAGE AREA - 31,736 S.F.
- (5B) EXISTING CART MAINTENANCE AREA - 64,806 S.F.
